

Nov. Financial Review

Dec. 17, 2012



101 Fluids and Combustion Facility, MIP & TSC



ZIN Manager: Michael Johanson

ZIN Engineering Lead: M.O'Toole

ZIN Operations Lead: T. Wasserbauer

ZIN Integration Lead: C. Rogers

NASA Program Manager: Tom St'Onge

NASA Project Manager: Bob Corban (Kevin McPherson)



SpaceDOC 101 encompasses the International Space Station (ISS) Fluids and Combustion Facility (FCF) Project and its initial payloads, Light Microscopy Module (LMM) and the Multi-user Droplet Combustion Apparatus (MDCA) have been launched and the flight units are installed on the ISS. The Flight units on the ISS, as well as the units on the ground (Ground Integration Units and the Engineering Development Units) need to be operated and maintained. This Delivery Order is for the operation of the FCF racks on orbit and on the ground, resolution of any anomalies, evaluation of trends, software upgrades, hardware obsolescence evaluation, new hardware development to support future capabilities, verification, and training the crew and operators on the hardware/software. Also, as new payloads are developed for the FCF, analytical modeling and engineering analysis of the interface will be required.



The CIR Flight Unit, along with MDCA, was delivered to the ISS by STS-126 (November 2008). The FIR Flight Unit along with the LMM were delivered to the ISS by STS-128 (August 2009).



Issue	Potential Impact	Action Plan	Resolution Date
Crew Time Availability	Delays in science data	Crew time request for bottle R&R filled. Crew time request for CIA igniter and fiber R&R filled	Resolved
CIR/FIR operations request is not fully supported by ISS resources or FCF operations budget	Loss of FIR/CIR Utilization	Operations assumptions and guide lines incorporated into 2013 statement of work.	Resolved

- **FLEX2 Science**
 - Continued the FLEX2 Quiescent/Convective Matrix
 - November total is 23 downlink test point ignitions
- **ACE Science**
 - Submitted operations inputs for the ACE-M-1 experiment expected to begin after launch of SPX2 in March 2013
- **Safety**
 - Soyuz Safety Data Package for FOMA Cal unit submitted to PSRP
 - SPX2 Return SDP submitted to PSRP
 - ATV Manifest SDP submitted to PSRP
 - HTV-4 manifest SDP drafted
 - GCIP SDP drafted
 - Drafted the GCIP Fracture Control Summary Report
- **Software**
 - Conducted ERB for on-orbit ISPU reformat procedure
 - Conducted ERB for LMM/ACE enhancement updates
- **Integration**
 - Coordinated manifest change for the GCIP and cables from ATV4 to HTV4 to meet safety schedule
 - Submitted HTV4 manifest request
 - Submitted FCF Life Extension Memo
- **LMM GIU - Completed closeout of all LMM GIU DO tasks**
- **Hardware deliverables**
 - Completed Vibration test of diagnostic h/w (IAM, DCM, LCTF, Focus Prism)
 - Approved waiver, rationale and EMI analysis for GCIP EMI test exceedence
 - Submitted EMI analysis & rationale for MDCA Avionics waiver to GRC

2012 Deliverables List

101 Fluids and Combustion Facility, MIP, TSC, LMM, MDCA

Deliverable	Planned	Actual	Note
Smoke Detector spare	Feb-2012	4/2012	
ATCU Fan Assemblies (2) spares	Apr-2012	4/2012	
ATCU Fan Filter Electronics Box spare	Apr-2012	4/2012	
EEU spare	Apr-2012	4/2012	
GCIP flight unit	Jun-2012		Assembly and test completed. Verifications in process, delivery for HTV-4 (Dec)
MDCA Avionics Package spare	Jun-2012		Assembly and test completed. Verification closure planned December
CIR Windows (2) spares	Jul-2012	3/2012	
LMM Control Box spare (No Environmental)	Jul-2012		Out of plan board vibe required. Out of plan power supply board re-build. PCB assembly complete planned December
QD Lubrication Kit (if required)	Jul-2012		Concept coordinated with ISS Qdirt. Final design pending program feedback
IPSU spare - Remora	Sep-2012		Assembly complete EMI test scheduled for December
Focus Prism spare	Nov-2012	11/2012	
DCM spares (2)	Nov-2012	11/2012	
ICM spare	Nov-2012	11/2012	
MDCA Color Camera spare	Nov-2012		EMI test re-schedule for January to accommodate SAMS EMI facility request
GIU LCTF	Dec-2012	11/2012	
Common IAM spare	Dec-2012	11/2012	

Risk Matrix - FCF

101 Fluids and Combustion Facility, MIP, TSC, LMM, MDCA




CONSEQUENCES

Criticality	L x C Trend
High	↓ Decreasing (Improving)
Med	↑ Increasing (Worsening)
Low	→ UnChanged
	* New since last month

Risk Id	Risk Title	Risk Statement	L	C	Approach
FCFSE-026 → Technical Beltram	LMM GIU does not fully emulate the flight unit	Given that the LMM GIU does not fully emulate the flight unit; the possibility exists that future LMM flight experiments will not operate correctly.	3	3	Mitigate: Plan is to review LMM GIU non-flight design issues, and add task to update LMM GIU to the next DO period of performance. Status: 12/21/11 - Task has been added to the DO to upgrade to LMM GIU. 01/11/12 - No updates at this time. 02/17/12 - The LMMGIU has been assessed and the upgrades needed to emulate the flight system have been identified. Additionally, microscope motor functions are in the process of being repaired. 03/28/12 - Risk has been reviewed and there are no changes to its status at this time. 04/23/12 - Currently preparing trouble shoot procedures for LMM motor functions. 06/18/12 - This risk was reviewed and there are no updates at this time. 07/27/12 - Turret motor problem diagnosis has been completed and repair for it is in process. ECD: 07/02/2012
FCFSE-029 * Technical O'Toole	ICM failure	Given that the ICM may fail; then there will be a significant impact to the back lit imaging science instrument to occur.	3	3	Mitigate: Develop ICM spares. Status: ECD: 04/30/2013
FCFSE-014 ↓ Technical Beltram	IOP removable hard drive shelf life	Given that the IOP removable hard drives have a limited shelf life; then there is the possibility that these hard drives won't work over time and the FIR and CIR racks will not be able to provide support for their payloads to perform science operations will occur.	2	3	Mitigate: Implement a procedure to re-format the hard drive on-orbit to minimize loss of magnetic field encoding data on the disk. Status: 04/23/12 - Currently on track for the development of the formatting procedure. 06/18/12 - This risk was reviewed and there are no updates at this time. 07/27/12 - Formatting being developed. 09/12/12 - Documented format procedure is in process of being developed. ECD: 08/30/2013

7



CONSEQUENCES

Criticality

High (Red)

Med (Yellow)

Low (Green)

L x C Trend

↓ Decreasing (Improving)

↑ Increasing (Worsening)


→ UnChanged

* New since last month

Risk Id	Risk Title	Risk Statement	L	C	Approach
MDCA-012 ★ Technical O'Toole	FLEX-2J Droplet Size Repeatability	Given the tolerance on droplet reproducibility has not been demonstrated there is possibility that we will not meet the reproducibility requirement	4	3	Mitigate: Review science requirement with JAXA and determine the capability of the flight hardware to meet the science requirement. Status: 06/18/12 - Not started. S/W engineering resource not available as of 6/15/2012. Expected closure date is Aug 31, 2012. 09/12/12 - Awaiting for the revised MDCA S/W to complete the last mitigation task. ECD: 10/31/2012
MDCA-011 ★ Technical O'Toole	FLEX-2J Deployment Validation	Given that we cannot verify multiple droplet deployments in a 1G environment there is possibility that not all science will be met	3	4	Mitigate: Develop a robust 1G validation program Status: 06/18/12 - Not started. S/W engineering resource not available as of 6/15/2012. 07/27/12 - S/W developer resource got a late start. 09/12/12 - Pushed out the first mitigation task by one month per monthly RMWG. ECD: 10/31/2012
MDCA-007 ★ Cost O'Toole	Lack of on-orbit spare avionics box	Given that there is no flight spare MDCA avionics box on ISS and there are no plans or budget to build a flight or GIU MDCA avionics box; then there is the possibility that, if the MDCA avionics box becomes inoperable, a complete loss of the ability to obtain FLEX-2 science will occur.	2	5	Mitigate: A plan to build a flight spare avionics package is authorized under the current DO with delivery planned for the 4th quarter of 2011. Status: 08/24/11 - Still on schedule to deliver flight spare avionics box. 10/04/11 - The project is still targeting the flight spare avionics delivery in December of 2011. 11/15/11 - Delivery of the assembly is projected for February 1, 2012. Verification and manifest is expected to be included in the follow-on DO period of performance. 03/07/12 - Flight spare MDCA avionics box is in the process of being built per ZIN Tech MWO. 03/28/12 - Flight spare avionics box is tentatively scheduled for several environmental tests as follows: Vibe & EMI in May of 2012 and Thermal Cycle in June of 2012. 04/23/12 - Flight spare avionics box is in the process of being built. 06/18/12 - Assembly complete. Vibration and EMI testing Completed. Thermal Cycle testing scheduled for June 2012. ECD: 09/28/2012

Risk Matrix - FCF

101 Fluids and Combustion Facility, MIP, TSC, LMM, MDCA

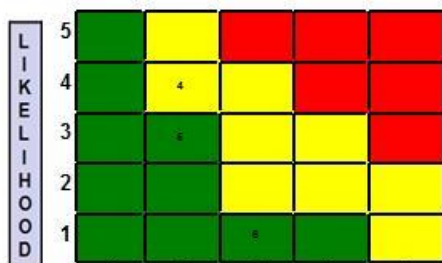

CONSEQUENCES

Criticality

High

Med

Low

L x C Trend

↓ Decreasing (Improving)

↑ Increasing (Worsening)


→ UnChanged

★ New since last month

Risk Id	Risk Title	Risk Statement	L	C	Approach
MDCA-013 ➡ Technical O'Toole	FLEX-2J Droplet Imaging Resolution	Given that there is limited performance data for the droplet imaging camera at 60 frames per second there is possibility that we will not meet the resolution requirement	4	2	Mitigate: Review science requirement with JAXA and determine CIR h/w capability. Status: 06/18/12 - Resolution test pending 60 fps camera configuration. Initial attempt to operate at 60 fps failed. Expected closure date is Aug 31, 2012 per O'Toole's e-mail Friday 6/15/2012. 09/12/12 - Demonstrated that there is a 60 fps capability. The resolution test still needs to be done. ECD: 08/31/2012
MDCA-010 ➡ Schedule O'Toole	FLEX-2J SRD not signed	Given that the FLEX2J SRD is not signed at PDR there is a risk that project cost and schedule will not be met.	3	2	Mitigate: Document requirements as understood via previous TIMs and coordinate with JAXA to obtain concurrence Status: 06/18/12 - Reviewed updated draft document with JAXA rep. Signature parties identified per O'Toole's e-mail Friday 6/15/2012. 07/27/12 - FLEX-2J is still in work by the PI. Latest JAXA comments have been incorporated into the SRD. 09/12/12 - GRC Science, JAXA Science, as well as GRC Project management & Zin Engineering have all signed off on SRD. Awaiting for NASA HQ to sign off and approve. ECD: 09/28/2012
MDCA-014 ➡ Technical O'Toole	ICE-GA combustion by-products	Given that the hexanol combustion by-products are not established there is the possibility that the ICE-GA hexanol fuel may not be allowed on ISS.	1	3	Mitigate: The project intends to perform by-product testing on hexanol to show it is compatible with ISS vents requirements and meets toxicity limits. Status: 09/12/12 - Test has been initiated. ECD: 10/31/2012

Risk Matrix - FCF


101 Fluids and Combustion Facility, MIP, TSC, LMM, MDCA

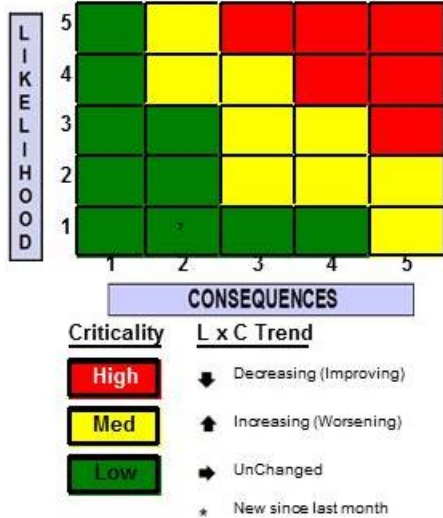

Risk Id	Risk Title	Risk Statement	L	C	Approach
MDCA-015 Schedule O'Toole	Unapproved ICE-GA Science Requirements Document	Given that the ICE-GA SRD is not signed at PDR there is a risk that project cost and schedule will not be met.	1	2	Mitigate: Get the SRD signed by both Italians and Project. Status: ECD: 09/28/2012

Risk Matrix - FCF

101 Fluids and Combustion Facility, MIP, TSC, LMM, MDCA

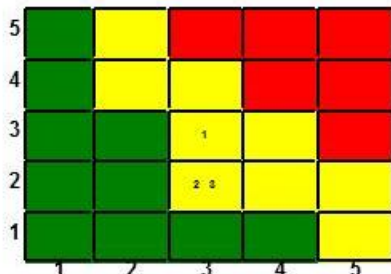


Criticality



L x C Trend

Decreasing (Improving)
Increasing (Worsening)
UnChanged
New since last month

Risk Id	Risk Title	Risk Statement	L	C	Approach
TSC-004	Lack of support depth	Given that there is no more than 1 subject matter expert in the areas of TSC System administration, FCF Ground software, and FCF data post-processing, there is a risk that FCF will not be supported adequately to ensure mission success.	3	3	Status: ECD: 12/28/2012
Cost					
TSC-002	DICES III voice loop system obsolete	Given that DICES III system hardware is at end-of-life, there is a risk that voice loop services will not be available to support mission operations.	2	3	Status: ECD: 12/28/2012
Technical					
TSC-003	Video System Difficult to Support	Given that the Grass Valley video matrix and AMX video switch system uses an unmaintainable and undocumented configuration, there is a risk that all video channels may not be available to support mission operations.	2	3	Status: ECD: 12/28/2012
Technical					

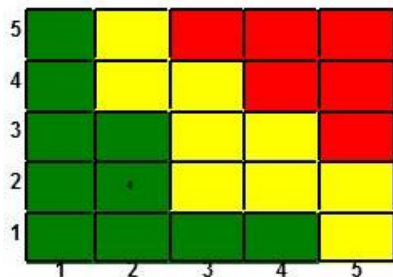

Risk Id	Risk Title	Risk Statement	L	C	Approach
TSC-001	Stale TSC documentation and not up to date	Given that documentation has not been updated as physical changes are made at the TSC, there is a risk that troubleshooting and maintenance will not be properly performed.	2	2	Status: ECD: 12/28/2012
Technical					

Criticality



L x C Trend

- Decreasing (Improving)
- Increasing (Worsening)
- UnChanged
- New since last month

102 Acceleration Measurement Program (AMP)

Engineering Lead Jennifer Keller & Ray Pavlik

NASA Program Manager: Tom St. Onge

NASA Project Lead: Kevin McPherson / Bob Hawersaat



SAMS Objective:

- Provide acceleration measurement systems that meet the requirements of the researchers on board the International Space Station.
- SAMS measures the acceleration environment in the 0.01 to 400 Hz range for payloads.

MAMS Objective:

- Provide acceleration measurement system that measures the Quasi steady and vibratory acceleration data in the 0.00001 to 100 Hz frequency range on board the International Space Station (ISS) vehicle

PIMS Objective:

- Provide acceleration measurement data to Principal investigators who conduct scientific research on board the International Space Station.
- The SAMS acceleration measurement system provides the raw data that PIMS uses to provide analysis to the Principal Investigators. SAMS measures the acceleration environment in the 0.01 to 400 Hz range for payloads.



WBS	Milestone	Start	Baseline	Projected	Actual	Schedule Variance
1.8.9	SE Cable – at least 144 inches in length	7/12		12/12		
1.8.10	Spare TSH-ES and TSH-ES 08 for MSG	7/12		12/12		


Issues and Concerns

102 AMP (SAMS, MAMS, PIMS)

Issue	Potential Impact	Action Plan	Resolution Date
Network issues onboard delaying EE-F05 boot process	EE-F05 not booting	Work with DMC to help determine network issues.	Moved sensor back to EE-F05 and the network troubles have not appeared as of late. Continue to work with Express if/when it does occur.
Crew office cannot properly torque the SAMS MSG baseplate into the MSG WV	Not a good surface mount for the SAMS TSH-ES	<ol style="list-style-type: none"> 1. ECO the SAMS AIDD to call out the torque values for the baseplate 2. Request in writing the issue and why it cannot be performed. 	<p>9/15/09 – telecon held with MSG. It was decided that the fasteners on the SAMS baseplate for the TSH-ES will not be torqued. Integrated Safety Hazards are being updated on the MSG side, and SAMS is clarifying a SAMS safety hazard.</p> <p>TSH installed in MSG and working with SODI. Crew procedures said to be hand tight.</p>

Top Risks

102 AMP (SAMS, MAMS, PIMS)

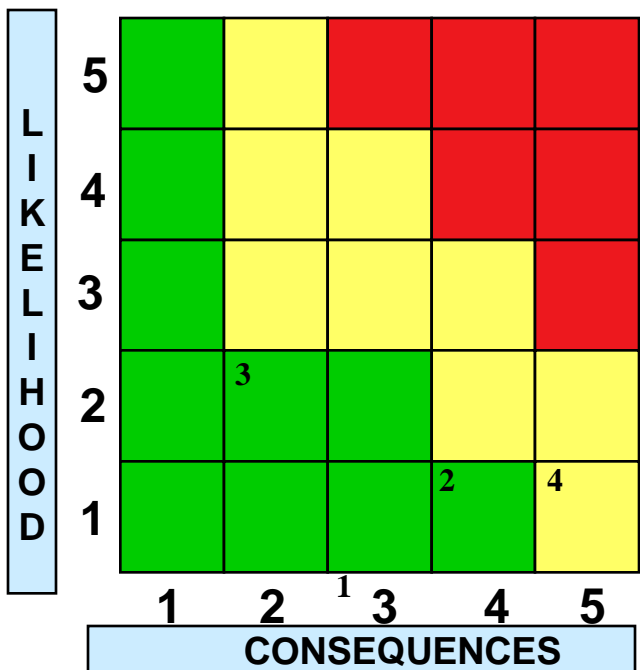

Criticality	LxC Trend	Approach
High	Decreasing	M-Mitigate
Med	Increasing	W-Watch
Low	Unchanged	A-Accept
	New	R-Research


Approaches: Mitigate, Watch, Accept, Research

Risk ID	Risk Title	Risk Statement	L	C	Approach
DO102-1	TSH-ES wire size	Wire sizing could limit usage of the TSH-ES. The use of 12 gauge wire would increase the size of the TSH. Many power suppliers have 20 amp breakers.	1	2	Watch: Will address risk with inline breakers if a customer requires it. Not a problem for FIR or CIR. Status: Does not affect FCF or MSG. Will address when there is a user. Close date: Future User
DO102-2	Commanding Issue	NCR 237 identified: The laptop may lockup when commanding to the TSH-ES that is running at 400 Hz.	2	3	Watch: The system will need to be rebooted only. Alternative means to address this issue in future software builds will be considered. 400 Hz mode not a normal operating mode. Status: Waiting for funds to consider s/w fix Close date: On going
DO102-3	SAMS Sparing	SAMS PCS hardware not supported by the ISS program.	3	2	Mitigate: Ghosting function for hard drives in place. Laptop shells, spare hard drives and floppy drives have been set aside on ISS for SAMS use. Status: Need to configure one more set of spare hard drives Close date: 04/09
DO102-4	SAMS Fan Regulator	SAMS RTS Drawer #2 fan regulator frequency varies	2	4	Watch: Fan speed has shown the variable frequency for several months and has not shown any distinct changes in behavior over that period of time. Status: Need to configure one more set of spare hard drives Close date: 04/09


November 2012




s-Flame
(drop test)

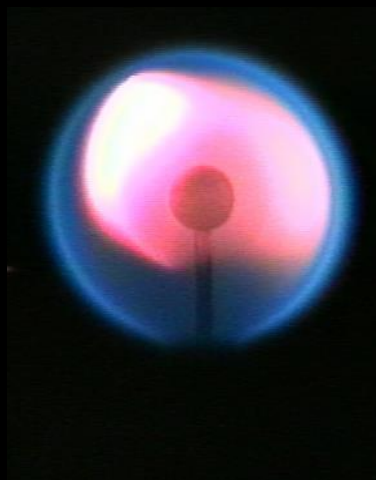

Flame Design
(drop test)

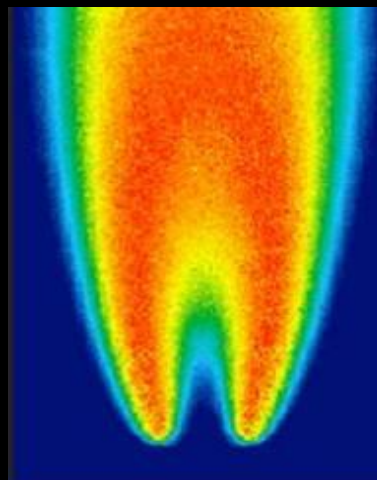

CLD Flame
(aircraft test)

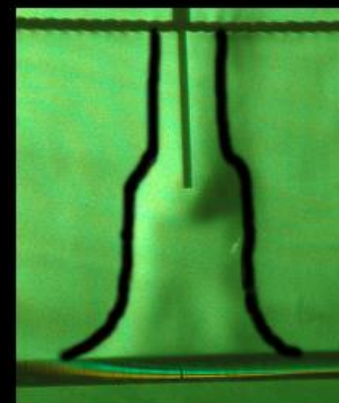

2850 V

E-FIELD Flames
(1g schlieren)

Manager: Brian Borowski

NASA Program Manager: Tom St. Onge

NASA Project Lead: Mark Hickman

NASA Project Scientist: Dennis Stocker

SpaceDOC 110 encompasses the initial development phase of ACME including requirements and verification development and planning, flow system breadboard interface with existing FOMA breadboard and color camera trade studies to ultimately provide a new diagnostic capability for CIR. Work on Engineering Model design is included following completion of Preliminary Design Review in January of 2011.


Issues	Potential Impact	Action Plan	Resolution Date
Coming out of the Phase 0/1 Safety Review there are some potential programmatic impacts involving materials, basic design elements and test matrices	Could result in changes to the design and/or test matrices	Project Scientist has been informed of areas of concern and will address and baseline the test matrix . Materials concerns are being re-assessed	4/12 Project Scientist has addressed the potential impacts. Decisions are now at a programmatic level
Following functional testing of the E-Field Subsystem and EMI testing of the same subsystem some requirement compliance issues have arisen with regard to rise times and energy levels	Unable to meet science requirements	Review Board has been convened to further discuss and provide guidance to management	12/12

- Continued build of EM Avionics Package
- Continued build of Flight Avionics Package
- Build of the EM Cube assembly underway, completion of this assembly is the Project Milestone for December 2012
- Completed October Project Milestone on October 30, 2012
- Completed November Project Milestone on October 31, 2012

WBS	Milestone FY12	Credit	Start	Baselined	Projected	Actual	Scheduled Variance
1.1	Interim Design Review	100% package complete	May 2012	June 2012		June 2012	



Task Level Risk Assessment

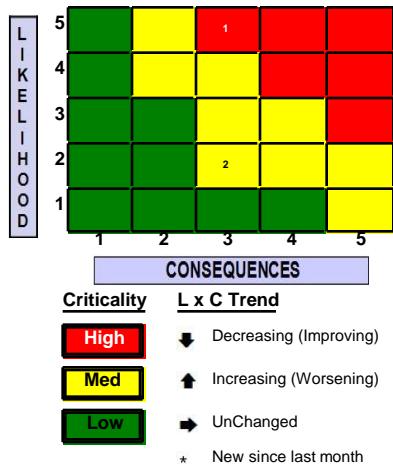



Risk Id	Risk Title	Risk Statement	L	C	Approach
ACME-014 Technical Rogers	IPSU to IOP image transfer rates take too long	Given that the current data transfer rates from the IPSU to the IOP is severely limited, transfer of ACME data may take an unacceptable amount of time and may reduce obtainable science for the allotted operational time on board ISS.	5	3	Watch: Need to keep an eye on this and follow up with the CIR team to keep updated on transfer improvements. Status: 12/13/11 - The FCF team has improved transfer rates by utilizing both IOP hard drives. The FCF team needs to provide quantitative data transfer rates. 03/27/12 - Risk reviewed by the ACME team and no status updates at this time. 05/08/12 - ACME RMWG has reviewed this risk and there are no updates at this time. 06/12/12 - Risk was reviewed at the monthly ACME RMWG and there are no updates at this time. 07/27/12 - Negotiations to fund an IPSU upgrade with increased data transfer rates has been initiated. 09/12/12 - Currently the IPSU to IOP transfer rate is approx 1.3 Mbps. The IPSU redesign concept calls for a direct downlink from the IPSU directly to ground with ISS downlink capability at 20Mbps. FCF project is submitting a funding request to support development of the concept. 09/18/12 - ACME needs a minimum of 10 Mbps. 10/16/12 - This was reviewed in the monthly RMWG with nothing new to report. 11/20/12 - The FCF NASA PM has obtained funding for a new IPSU design with the ACME data transfer rates as part of the design criteria. ECD: 12/31/2012
ACME-008 Technical Gobeli	E-field emission exceedences	Given that there might be e-field exceedence emissions; then there is the possibility that the EMI requirement will not be met and ACME hardware would be adversely effected causing diminished science to occur.	2	3	Mitigate: The ACME team will be intensively working with the EMI lab to determine what if any EMI exceedences occur to meet its EMI requirement and minimize any impact on the hardware. Status: 1/11/11 Planned testing has been delayed due to funding. 11/23/10 No changes or updates at this time. 9/14/2010 No changes or updates at this time. 05/03/11 - 5/3/2011 - This risk will be on hold until the Engineering Model is completed. 05/31/11 - 5/31/11 - Nothing new to report. 02/14/12 - Still appear to be on target for test date. 06/12/12 - EMI testing has begun and should be completed by the end of June 2012. 08/21/12 - EMI report # GRC-EMI-RPT-331 has been written. 09/18/12 - ACME Project Scientist is in discussions with the ACME team about potential

119 Ares V Payload Shroud Element (PSE) Project

ZIN Manager: Michael Johanson

ZIN Engineering Lead: Bill Dial

NASA Project Manager: Gerry Sadler

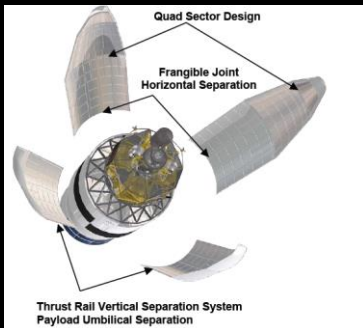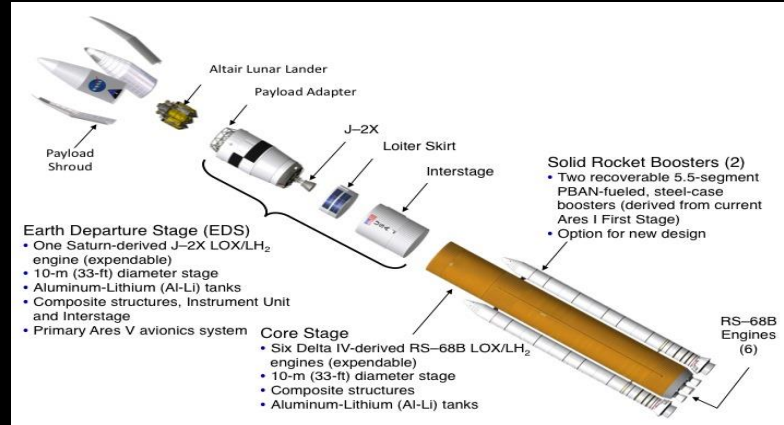

SpaceDOC 119 encompasses evaluation of potential manufacturing approaches focusing on the Heavy Lift Payload Shroud but not be limited to (e.g. can include other element composite dry structures). Approaches may include: existing composite manufacturing sites, MAF, and new sites. ZIN and our subcontractor Zero Point will identify needed composite manufacturing assets and capabilities to support current Heavy Lift Vehicle concept and associated requirements based on manufacturing assessments done by the NASA ESMD ACT project. The scope of the analysis shall include logistics and supply chain requirements.

Milestone Schedule

119 Ares V Payload Shroud Element (PSE) Project

Milestone (Cal 10)	Baseline (Cal 10)	Projected	Actual	Schedule Variance
Payload Shroud Technology Development Plan	November 30, 2010	Nov 30, 2010	Nov 30, 2010	None
Preliminary Element Integration Assessment Report	January 15, 2011	Jan 15, 2011	Jan15, 2011	None
Manufacturing Implementation Plan	February 15, 2011	Feb 15, 2011	Feb 15, 2011	None
Final Element Integration Assessment Report	March 25, 2011	April 25, 2011	April 25, 2011	1 month no cost extension approved by Gerry Sadler
Provide a Basis of Estimate Bottoms Up Assessment of the Current SLS Shroud for metallic and composite 8.4 meter baselines.	June 6, 2011	June 6, 2011	June 6, 2011	None
Assessment of CPS Impacts on Payload Shroud	September 30, 2011	Sept 30, 2011	Oct. 13, 2011	Delivery slipped based on stop work due to lack of funding, slip was approved by Gerry Sadler
Fairing Basis of Estimate Updates 1. PPBE13 Update 2. Initial PPBE14 Update 3. Final PPBE14 Update	1. Oct. 30, 2011 2. May 30, 2012 3. Sep 30, 2012	1. Oct. 30, 2011 2. May 30, 2012 3. Sep 30, 2012		The PPBE schedule is determined by NASA and the dates of the deliverables are subject to change.
Analysis and Design Reports 1. SRR 2. SDR	1. Oct. 1, 2011 2. Feb 1, 2012	1. Feb 1, 2012 2. Feb 1, 2012		SLS SRR & SDR are NASA determined dates. They are currently planned to be combined and held Feb. 15, 2012.
Payload Fairing Evaluation: Test Plans and Procedures	15 day prior to testing			None
Delta IV Stage Integration Assessment	Jan 31, 2012	Jan. 31, 2012		None

Study Delivery Order – No risks



Project Manager: Chris Sheehan




SpaceDOC 126 continues the work performed under SpaceDOC 113 to manufacture and flight verify the CSM/Glenn Harness as a crew preference item. Additionally, this delivery order carries drawing and documentation build information and materials research to allow for removal of the SDTO containment bag

EVM Milestone Schedule

126 Human Health Countermeasures (HHC)

WBS	Title	EVM Method	Start Date	End Date	EVM Plan
1.1	Management				
1.1.1	Project Management	LOE	6.01.11	5.31.12	8.3%/month
1.1.2	EVM/Cost Reporting	LOE	6.01.11	5.31.12	8.3%/month
1.1.3	Configuration Management	LOE	6.01.11	5.31.12	8.3%/month
1.1.4	Property Management	LOE	6.01.11	5.31.12	8.3%/month
1.1.5	Shipping and Receiving	LOE	6.01.11	5.31.12	8.3%/month
1.1.6	Purchasing	LOE	6.01.11	5.31.12	8.3%/month
1.3	Product Assurance				
1.3.1	Quality Management	LOE	9.14.11	5.8.12	12.5%/month
1.7	HHC Final Design and Fabrication	LOE	6.01.11	5.31.12	8.3%/month
1.8	System Assembly, Integration, Test and Launch	LOE	9.21.11	5.22.12	12.5%/month

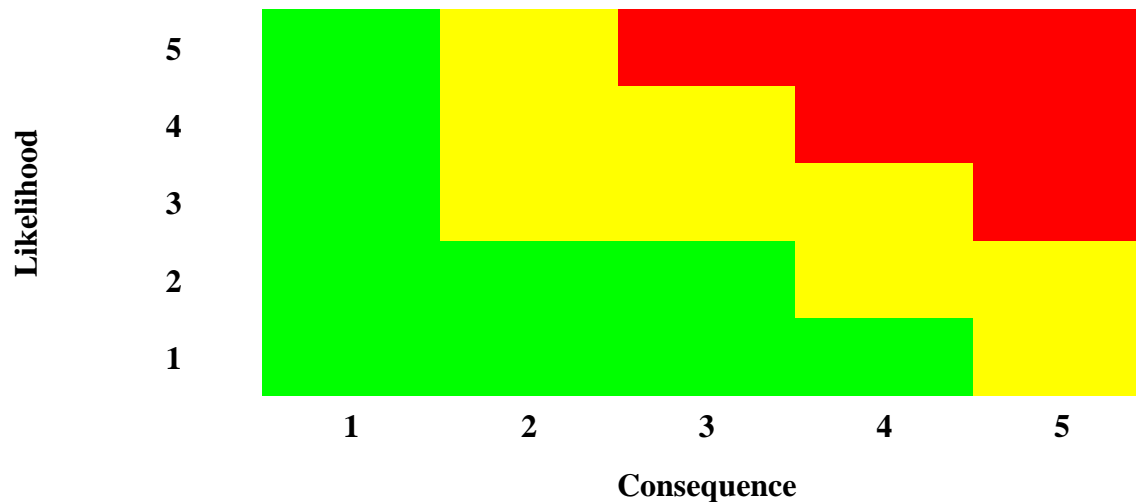

NO RISKS IDENTIFIED AT THIS TIME

Trend Legend

⬆ Upward

⬇ Downward

➡ No Change

■ New

Issue	Potential Impact	Action Plan	Resolution Date
None	-	-	-

DO-128 Communications, Navigation, and Networking Reconfigurable Testbed (CoNNeCT-2)



ZIN Project Lead: Ray Pavlik
ZIN Software Lead: Jennifer Keller

NASA Project Manager: Diane Malarik
NASA Deputy Project Manager: Mike Zernic
NASA GRC PI: Rich Reinhart
NASA GRC Deputy PI: Sandy Johnson

- An on-orbit, adaptable, Software Defined Radios (SDR)/Space Telecommunications Radio System (STRS)-based testbed facility to conduct a suite of experiments to advance technologies, reduce risk, and enable future mission capabilities on the International Space Station (ISS).
- DO-128 Scope of Work includes:
 - Performing configuration management activities, including software.
 - Remaining development of the CoNNeCT Flight and Ground System Software.
 - Integration with the Payload Operations Integration Center (POIC) and SCaN-provided SN, NEN, and NISN.
 - Sustaining Engineering and Operations of the Flight and Ground System.
 - Experiment Integration and Operation

Issue	Potential Impact	Action Plan	Resolution Date
None			

- Subtask A CM/DM
 - Reviewed, formatted, and released multiple Documents, Process Plans, Change Requests, and NCRs.
 - Supported GIU drawing updates.
 - Processed for storage as-run Mission Operations Procedures and GIU documents.
 - Completed all branch merges for the first flight Payload Avionics Software (PAS) update.
 - Reviewed and began updating the PAS Build and Release Procedure.
 - Generated a document that contains an explanation of the operation of SCan Avionics build scripts, their development history and user's guide-like information.
- Subtask B SE&I, Software, and Experiment Integration
 - GIU Maintenance (GRC-CONN-PLAN-0895)
 - Downloaded Avionics Files on a weekly basis.
 - Installed new Symantec Virus Definition Files on: GIU TReK Workstation, GIU GSE Terminal, GIU Laptop, and ELC SCS #2. Ran a full virus scan on all computers.
 - GIU GSE/TSE/TReK/ELC Network
 - Removed the GIU Laptop from the network. It retains its wireless capability for access to the NASA Guest Network.
 - The GSE/TSE Network was connected to the TReK/ELC Network allowing all computers to get their time from the Master Time Clock Unit in TEI #1. Currently the computers are using the Windows Time Server to achieve time synchronization.
 - GIU TWTA Pre Amplifier
 - The design was finalized. Design documentation was submitted to drafting with drawings due by late January.
 - Breadboard unit was installed on GIU to facilitate Harris Characterization.

- Subtask B SE&I, Software, and Experiment Integration (continued)
 - Experiment 25A TDRS-K
 - Conducted two TDRS-K integration telecons
 - Worked with the TDRS-K team to prepare final draft of the experiment plan. The plan was submitted to CM and released for formal review.
 - Supported TDRS-K dress rehearsal at the TSC. Several items were surfaced that will help improve the flow of the actual test. The GSFC TDRS K test lead was pleased with the results.
 - Wrote and installed a LabVIEW program (on KaTSIM Windows computer) to remotely control (transmit & standby modes) and query (output power (dBm & watts)) the Harris commercial TWTA.
 - Started trouble shooting the DAS backup and archival program, Zmanda, that collects the experiment data from the TEI's and KaTSIM. The program developed problems after a required equipment power down/up several weeks ago. It appears a startup file became corrupted. A temporary work around is being used to access the program and collect data until the corrupted file is found and repaired.
 - Ground Software
 - Worked on CRs for CTADS and CESDB updates.
 - Worked on the Store Telemetry And Retrieval System (STARS) requirements and design description
 - Worked on the CTADS User Guide and Version Description Document.
 - Flight Software
 - Created a rough draft of the regression test plan for the first flight PAS update. Sent out for internal review.
 - Identified new improvements for APS operations.

- Subtask B SE&I, Software, and Experiment Integration (continued)
 - Flight Software (continued)
 - Moved and temporarily setup SDS4 and supporting equipment at ZINO Software Lab. Prepared remainder of software development system equipment for relocation to ZINO Software Lab.
 - Provide ROM time estimates for PI requested software enhancements.
- Subtask C Flight & Ground Software
 - As of FY2013, flight and ground software activities have transitioned to WBS 01-03.
- Subtask D Mission Operations
 - Worked with PPM, Prep-OC, and TCO to add SCAN Testbed activities to timeline
 - Prepared weekly PPM inputs and the weekly POIC Briefing
 - Drafted procedures for the GD SDR Commissioning
 - Created Configuration Data Sheets for each week of Flight Operations. A new format was created to allow for more flexibility for the downloading and archiving of files. Initially it was thought that Fridays would be File Manager days and file transfers would be reserved for that day. With the coordinating of SN/NEN and POIC schedules it is becoming apparent that Friday's may be needed for experiment runs. This creates a condition where file management is "fit in" during normal operations.
 - Continued troubleshooting activities on the SFEP with GSFC personnel.
 - Mission Planning TCR: The TCRs (TDRS Contact Requests) were generated to support the pass planning for Weeks 08, 10, 11 and 12 for Increment 33 (Week 09 was a stand-down week). This involved multiple revisions to support ephemeris updates and reboost events.


- Subtask D Mission Operations (continued)
 - APS Commissioning – VTR Preparation: Completed the materials to support the APS commissioning activities. This included laying out a detailed test matrix of 39 graduated tests, various mission simulations using the LynxCAT SK Toolbox, and designing a detailed test schedule. The VTR was successfully completed. The LynxCAT SK Toolbox simulations were focused on creating the necessary closed loop configurations to support testing.
 - Provided SN and NEN resource schedule support from October 19 through November 23. In addition, worked with the Network Ops Manager in coordinating SN and NEN support for SCAN Tested APS Commissioning.

Hardware/Software Deliverables

No.	Item Description	Planned Completion Date	Actual Completion Date	Note
a)	Subtask A –CM/DM: Configuration Management and Tracking System (CMTS)	December 31, 2012		Hardware – this will transition to the next period of performance for this DO.
b)	Subtask C – Flt & Grnd SW: Verified Post-Ship Flight Software for subsequent upload to the Flight System	July 2012		Software – This has been rescheduled to December 2012.
c)	Subtask C – Flt & Grnd SW: Verified Ground Software required for JAXA Ground Processing	February 2012	February 2012	Software
d)	Subtask C – Flt & Grnd SW: Ground Software to support Mission Simulations	Q3 FY12	July 12, 2012	Software – Final Mission Simulation held 07/12/12.
e)	Subtask C – Flt & Grnd SW: Verified Ground Software, suitable for use during C/O & C	June 2012	August 2012	Software - SCaN Testbed operated for first time on-orbit on 08/13/2012.
f)	Subtask C – Flt & Grnd SW: Verified Ground Software, suitable for use with Post-Ship Flight Software	July 2012		Software – This has been rescheduled to December 2012.
g)	Subtask D – Mission Ops: Control Center Equipment for use during Mission Simulations and Mission	Q3 FY12	October 2012	Hardware – GPS System delivered 10/21/02
h)	Subtask D – Mission Ops: Data Distribution Services Software	May 2012		Software – Moved to December 2012 in order to capture lessons learned from C&C.

DO-128 Risk Matrix Overview

STATUS AS OF: 11/17/12

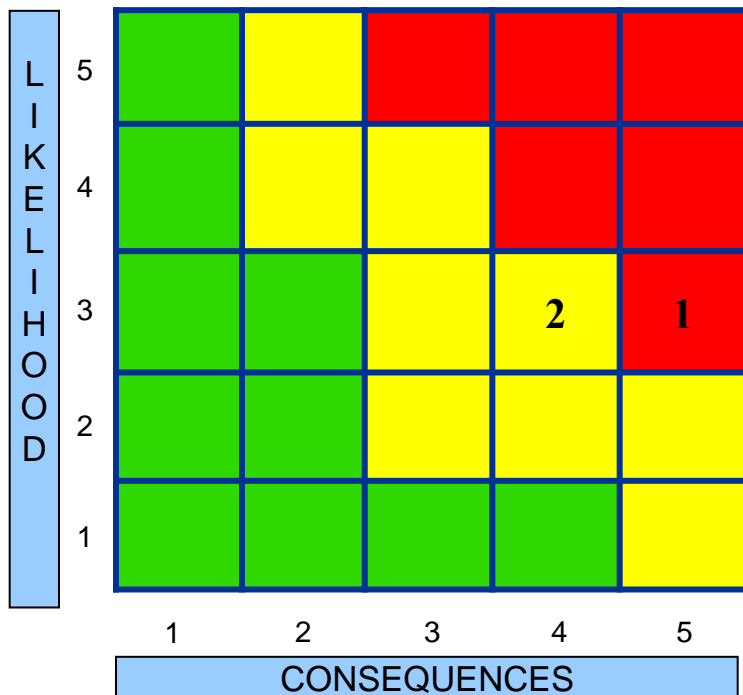

LxC Trend	Rank	Approach	Risk Title
→	1	M	Underfunded Operations and Experiments Phase
→	2	M	Experimenter Software Interface

Criticality	L x C Trend	Approach
High	↓ Decreasing (Improving)	M – Mitigate
Med	↑ Increasing (Worsening)	W – Watch
Low	→ Unchanged	A – Accept
	N New	R – Research
		C – Closed
